PRE-CONSTRUCTION SOIL TREATMENT GRAPH

Street address	City	State / ZIP	Date of application	Pages
212 Laurel Glen Court	Canton	GA 30114	10/27/2026	2

PT

Peachtree Termite & Pest Control
1480 Roswell Road, Suite 200
Marietta, GA 30062
(770) 555-0148
office@peachtreetermite.com

License no. 128419
Application 2 of 2
Permit no. BLD2026-04417

Builder or owner's agent	Builder phone	Lot and subdivision
Cherokee Ridge Homes	(770) 555-0137	Lot 14, Laurel Glen

Applicator	Registration or certification no.
Travis Coker	RE-38472

This application: ☐ Before the slab pour ☐ Foundation and backfill ☑ Final grade ☐ Other: _____

Type of construction: ☑ Slab ☐ Crawl space ☐ Basement

Linear footage of the structure	Total square footage of the structure	Termiticide	EPA Reg. No.	Finished dilution
228	2,304	Termidor SC (fipronil 9.1%)	7969-210	0.06%

Graph of the structure

Scale: 1 square = 3 ft

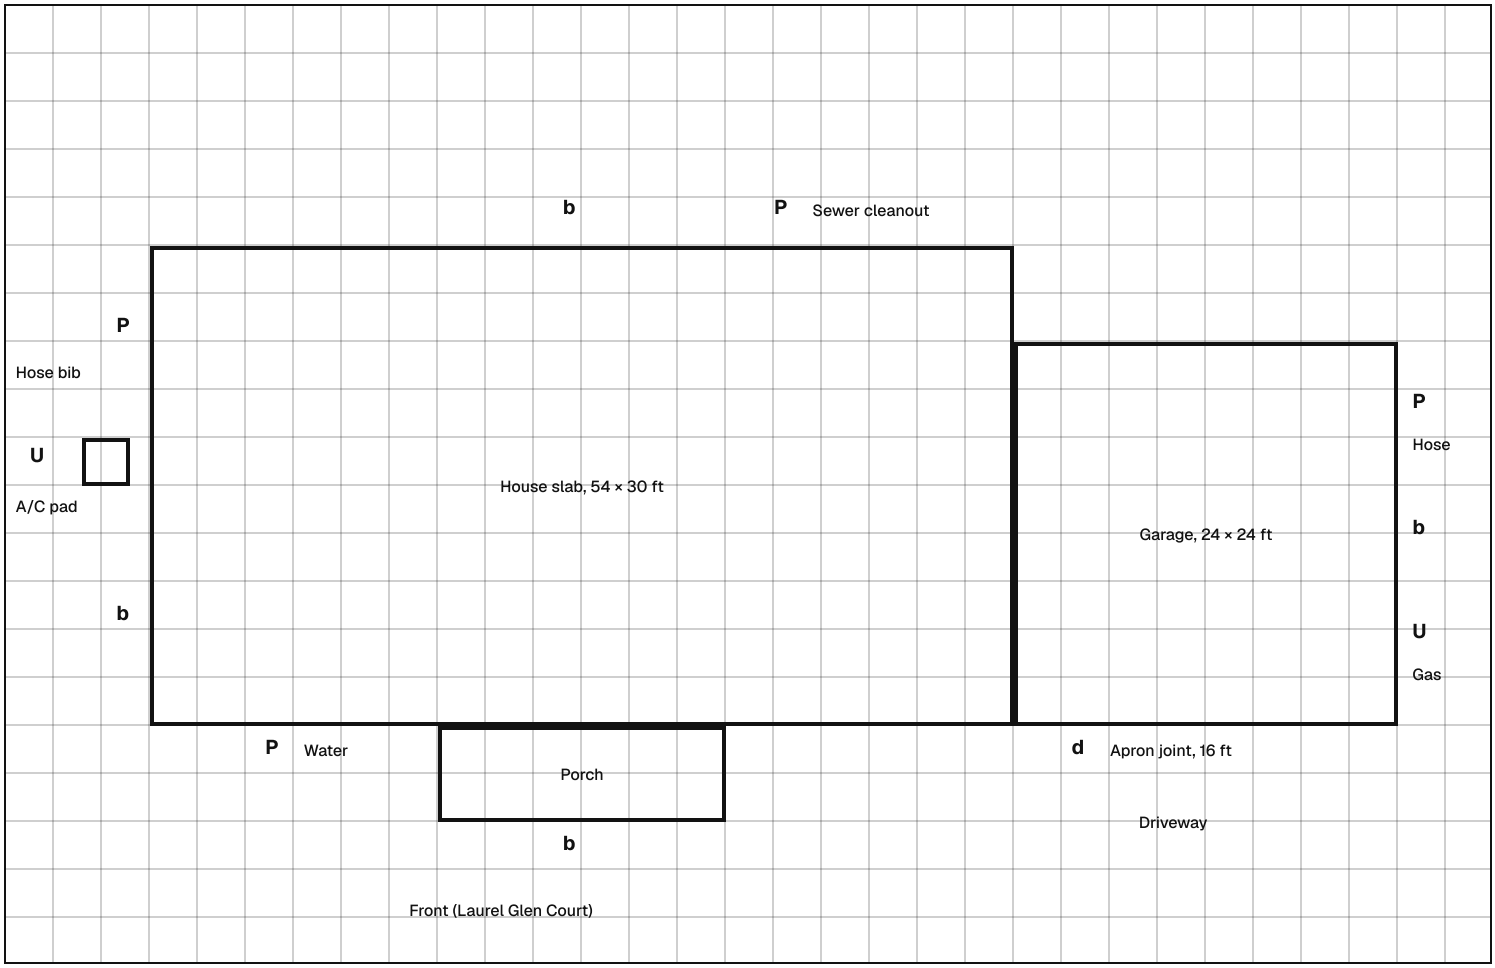

a to f Area in the volume table **U** Utility area **P** Pipe through the slab or wall —— Treated this application - - - Not treated this application

Property address:	Date of application:
212 Laurel Glen Court, Canton, GA 30114	10/27/2026

Volume applied to each area

Area treated	Linear ft	Sq ft	Depth (ft)	Rule's minimum rate	Minimum gal	Gallons applied
a Fill under slab				1 gal per 10 sq ft		N/A
b Trenches and backfill along foundation walls	212		1	4 gal per 10 lin ft per ft of depth	84.8	86
c Cavity walls, chimneys, hollow pillars				2 gal per 10 lin ft		N/A
d Pipes, expansion joints, other critical points	24		1	4 gal per 10 lin ft per ft of depth	9.6	10
e Utility areas	8		1	4 gal per 10 lin ft per ft of depth	3.2	4
f Other:						
				Total	97.6	100

Final application deadline

In all treatments, the final termiticide application must be completed within ninety (90) days after the earlier of:

- ☐ (I). the granting of a local "certificate of occupancy" or other like certification that the structure is approved for occupancy; Date _____
- ☐ (II). the actual occupancy of the structure by owner, tenant, or otherwise; Date _____
- ☐ (III). the closing of a permanent loan on the structure; or Date _____
- ☑ (IV). the completion of backfilling by the building contractor or owner. Date 09/22/2026

Final application due by:	This is the final application:	Earlier applications on this structure:
12/21/2026	☑ Yes ☐ No	No. 1 on 07/14/2026: fill under slab, 2,304 sq ft, 236 gal

Remarks

Final grade in place. Builder's superintendent told before the application, and the crew kept clear as the label asks. Mixed 100 gal at 0.06% (78 fl oz Termidor SC). Soil damp, no rain.

Applicator signature	Date
Travis Coker	10/27/2026

Rule 620-6-.04(2)(a)4(i): "For each application a separate graph of the structure showing the specific areas treated, including any utility areas, shall be prepared. Such graph shall indicate the linear footage of the structure, total square footage of the structure and the volume applied to each area."
